Gantt Chart - SouthCoast Wind Timeline of Major Permitting/Licensing Activities

6/9/2023

Federal & State	Major Permits	Filing Date
Federal		
BOEM	COP	2/15/2021
	Notice of Intent for EIS	11/1/2021
U.S. Army Corps of Engineers	Section 404/10 Permit	12/02/2022
U.S. Environmental Protection Agency	OCS Air Permit	11/23/2022
	NPDES- Offshore	10/31/2022
U.S. Fish and Wildlife Service	ESA Sec. 7 Consultation	3/9/2023
U.S NMFS & NOAA	MMPA - LOA	03/18/2022
	ESA Sec. 7 Consultation	7/21/23
State/Rhode Island		
RI Energy Facility Siting Board	License to Construct Filed	5/31/2022
RI DEM	401 Water Quality Cert. & Drg. P	03/17/2023
RI CRMC	Category B Assent	2/24/2023
	RI CRMC Consistency Statement	3/16/2022
State/Massachusetts		
MA Executive Office of Energy & Env.	MEPA ENF Certificate-Issued 10/11/2022	8/12/2022
MA Environmental Policy Act (MEPA)	MEPA DEIR Certificate	2/1/2023
	MEPA FEIR Certificate	7/3/2023
Massachusetts Energy Facilities Siting Board	MA EFSB	5/27/2022
MA Department of Public Utilities	DPU Approval to Construct/Zoning Exmp.	5/27/2022
MassDEP	Ch. 91 License/ WQC	Jun/Jul 2023
MA Office of Coastal Zone Mgmt.	MA CZM FCR Concurrence	1/13/2022
Other Key Dates & Notes		
Project Key Milestones	PPA/Construction Start Date	

Note: Project COD is currently 2028 but is subject to change.

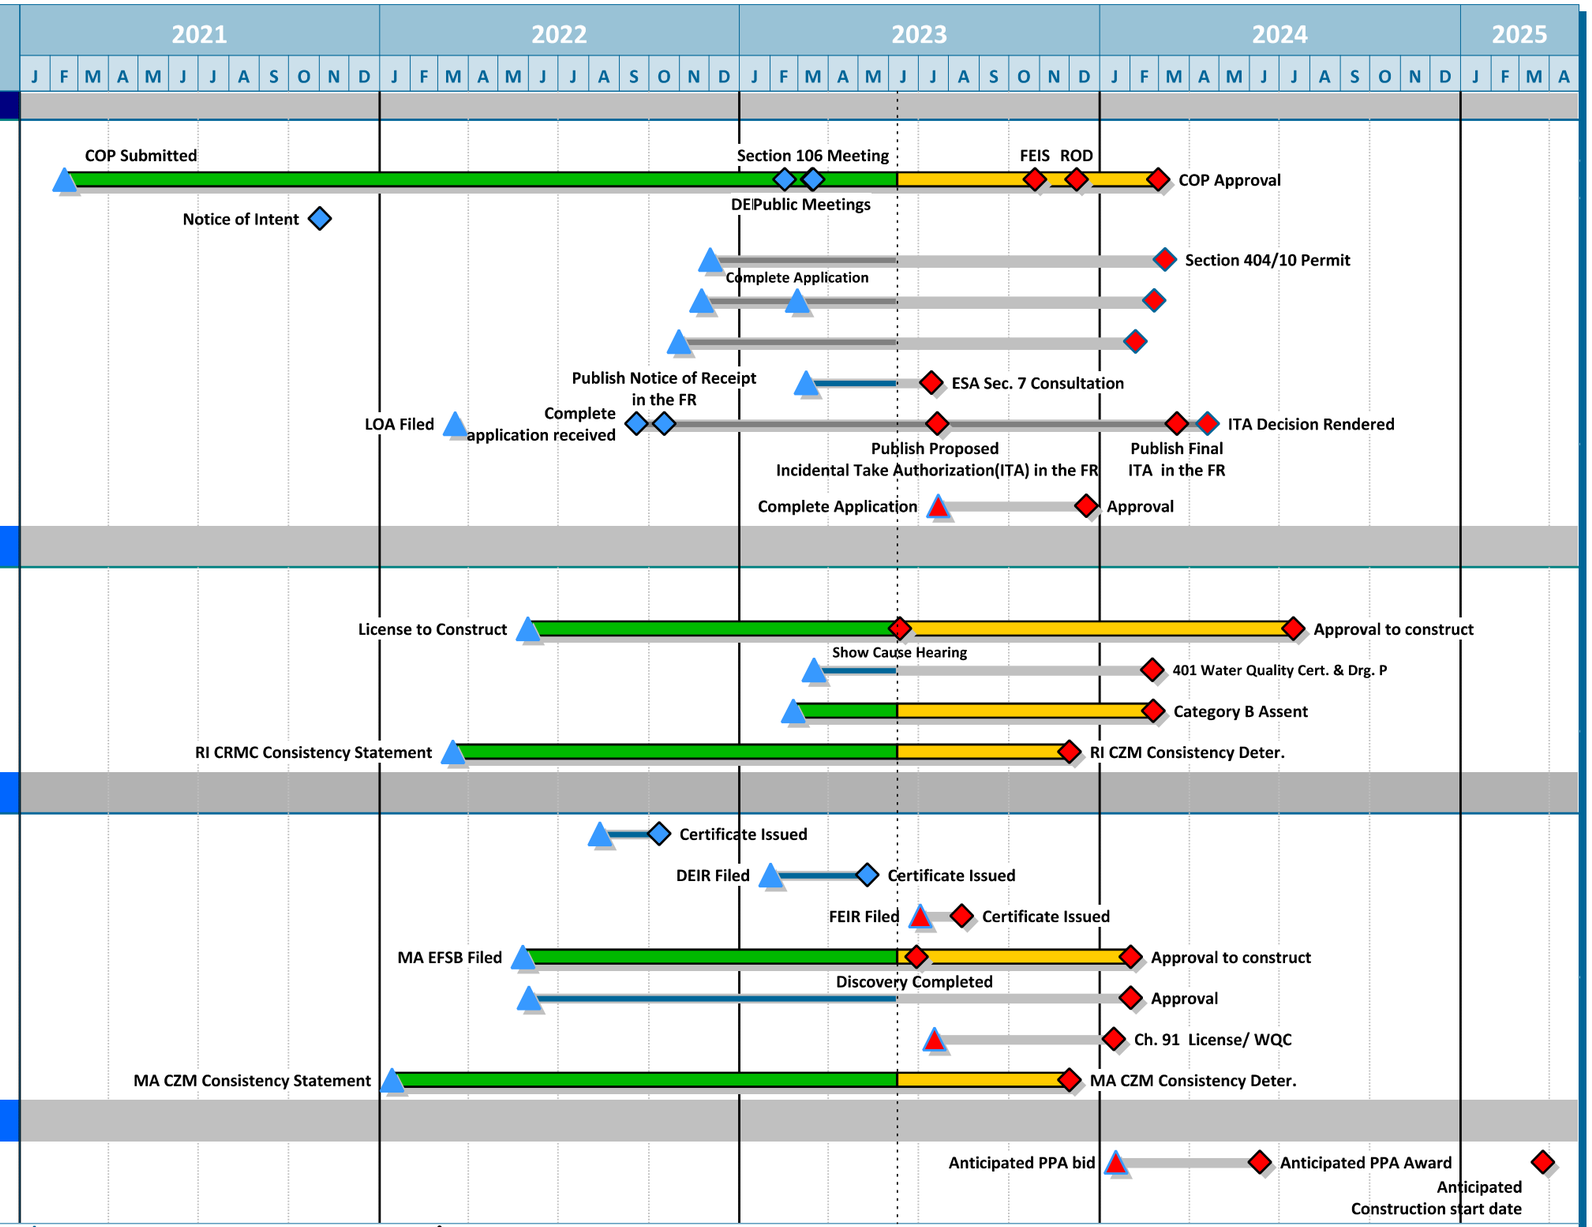

Start Date | Completed Milestone/Task | Anticipated Future Filing | Future Milestone/Approval
